

TEESWORKS

Remaining
COMAH
Inventory

COMAH Dangerous Substances Site Totals

Petroleum Products & Heavy Fuels (Gas Oils & Heavy Fuel Oil): 314.9T: **below Lower Tier qualifying limit**

H2 Acute Toxic (Crude Benzole): 31.21T: **below Lower Tier qualifying limit**

P7 Pyrophoric (Coke Oven Gas Main Deposits): 3,308.71T: **above Upper Tier qualifying limit**

E1 Hazardous to the Aquatic Environment (Gasholder Sealant & Naphthalene): 120.33T: **above Lower Tier qualifying limit**

E2 Hazardous to the Aquatic Environment (Benzole Absorbing Oil/Creosote & Coal Tar): 3,806.45T: **above Upper Tier qualifying limit**

Lower Tier	Upper Tier
≥2,500	≥25,000
≥50	≥200
≥50	≥200
≥100	≥200
≥200	≥500

South Bank Coke Ovens

- All major structures demolished.
- Cleaning of the gulley system has started.
- Presently stored in containers awaiting disposal:
 - Coal Tar
 - 66 IBCs (135 removed in September)
 - 4 drums
 - Heavy Fuel Oil
 - 4 IBCs
 - 6 drums
 - Coke Oven Gas Main Deposits
 - 51 IBCs
 - 235 steel drums




Decanting area for
COGM solids

Waste storage area
prior to removal from
site

Redcar Coke Ovens

- Majority of inventory still within tanks and vessels
- COGM washings (including deposits) stored in clarifiers at former BET plant
- Coal tar heel from BET Bay 3 in Acumen waste storage area
- Tar removed from Tar Tanks 2T106 and 2T107 stored in Acumen waste storage area

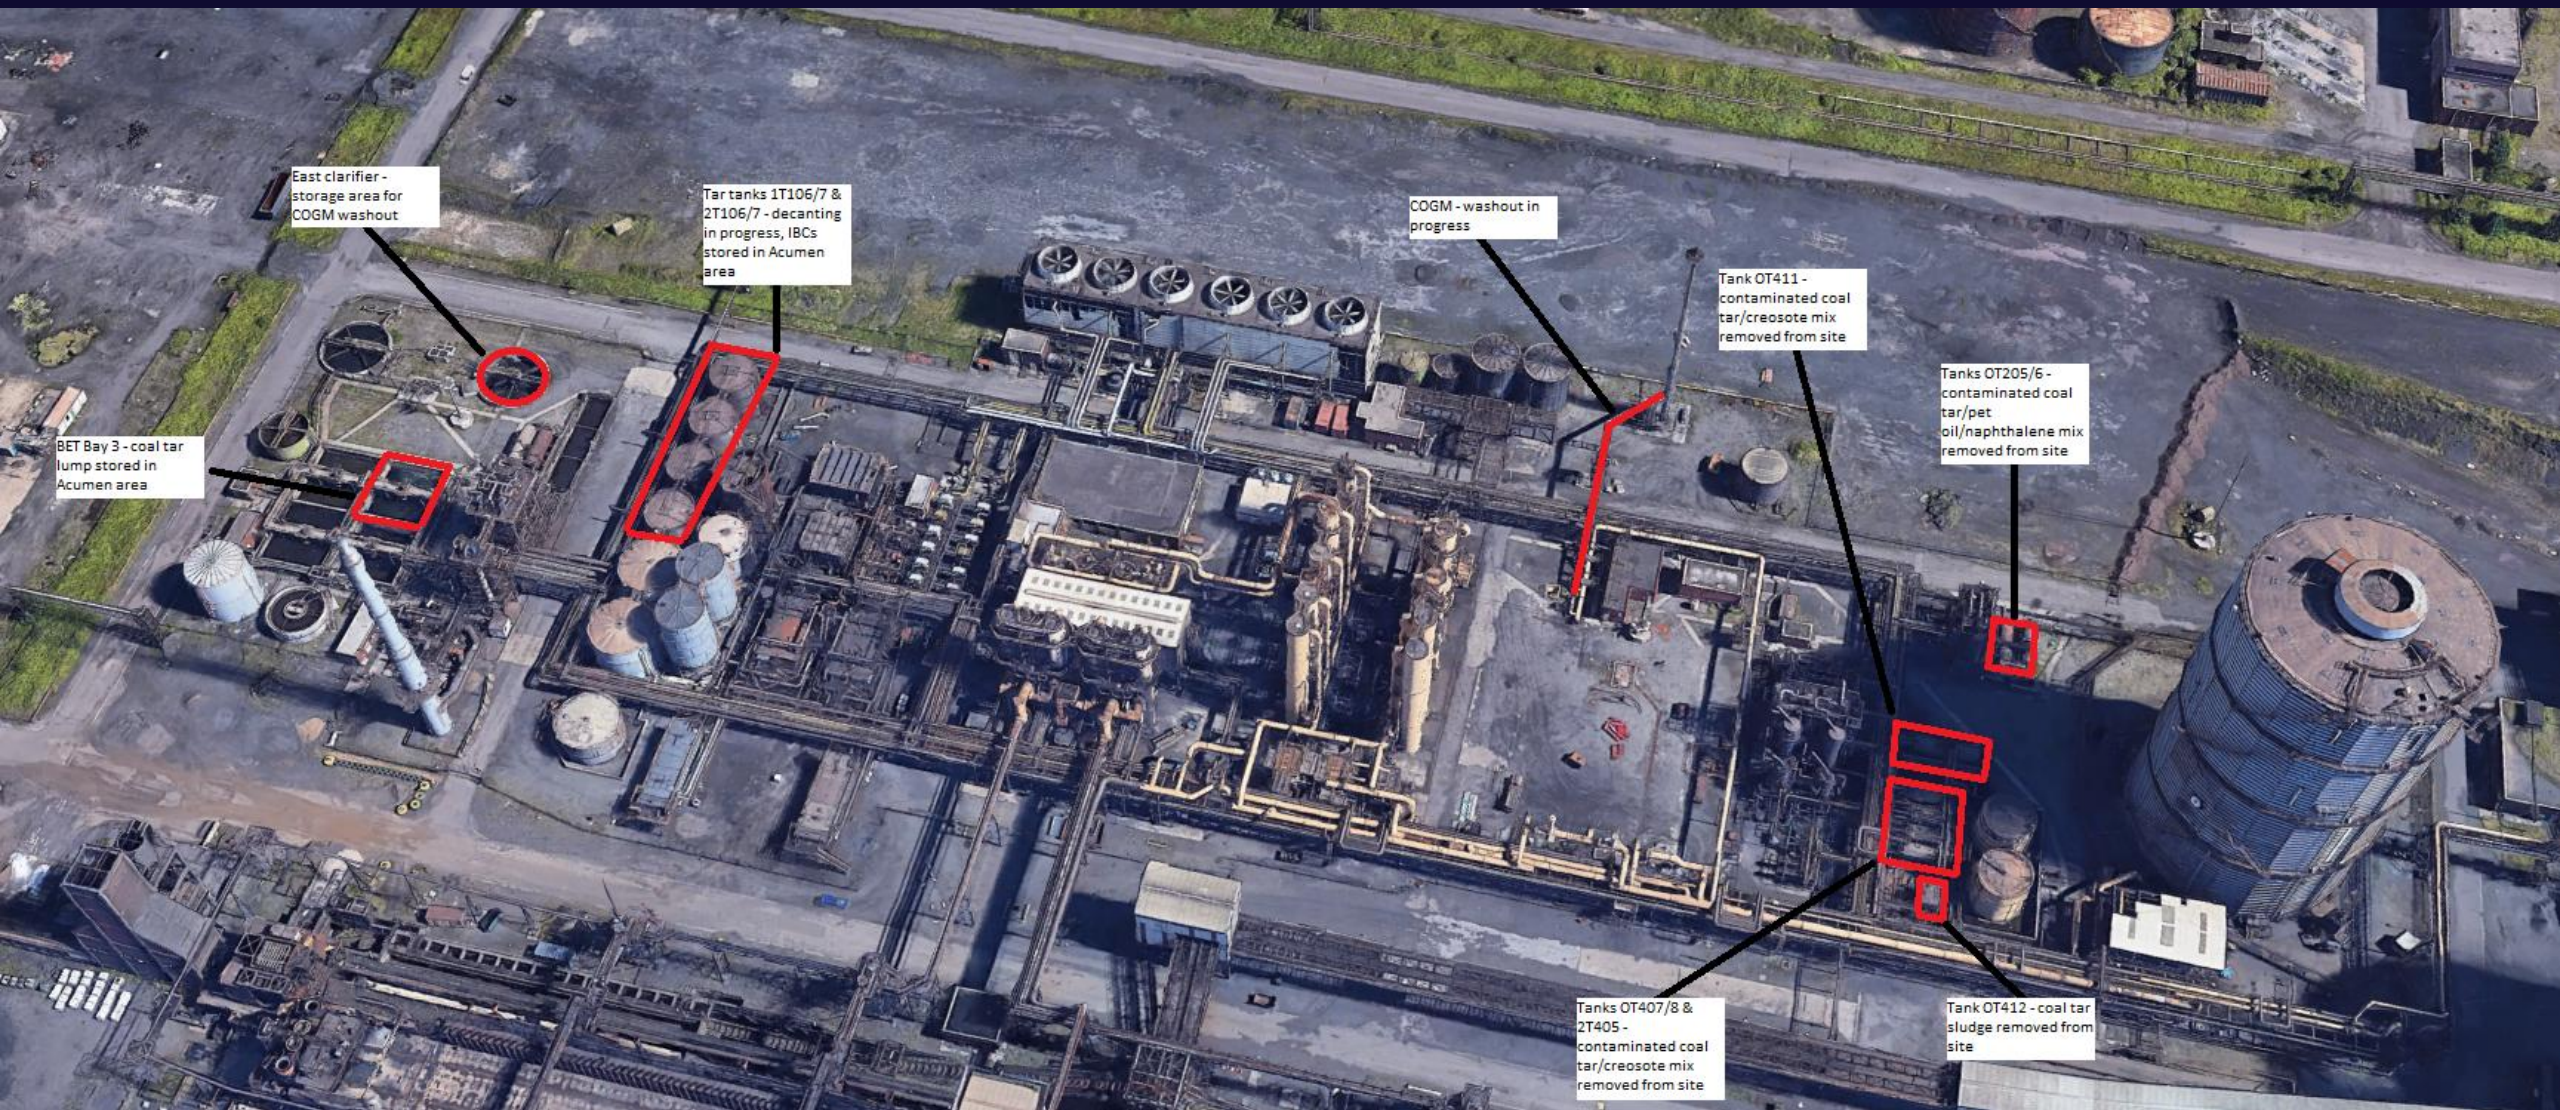

East clarifier -
storage area for
COGM washout

Tar tanks 1T106/7 &
2T106/7 - decanting
in progress, IBCs
stored in Acumen
area

COGM - washout in
progress

Tank OT411 -
contaminated coal
tar/creosote mix
removed from site

Tanks OT205/6 -
contaminated coal
tar/pet
oil/naphthalene mix
removed from site

BET Bay 3 - coal tar
lump stored in
Acumen area

Tanks OT407/8 &
2T405 -
contaminated coal
tar/creosote mix
removed from site

Tank OT412 - coal tar
sludge removed from
site

FSA

- All structures demolished with remaining inventory stored in IBCs and steel drums on old Butane Tank footprint.



IBCs/drums stored
on old Butane Tank
footprint prior to
removal from site


Redcar Blast Furnace

- Cleaning of COG Main and BFG Main complete, including feed to PCI Plant. Work ongoing on Pipe Bridges 21 and 22 (outside of TMO)
- Material taken to WSG storage area (Dye Pen Bay, Lackenby) for decanting into IBCs/steel drums prior to removal from site.



Iron Gran Plant

- 153 Pactec bags containing COGM solids previously stored at SBCO have been transferred to this area for storage. Transfrontier Shipment (TFS) application in progress. Now with German equivalent of the Environment Agency for approval.

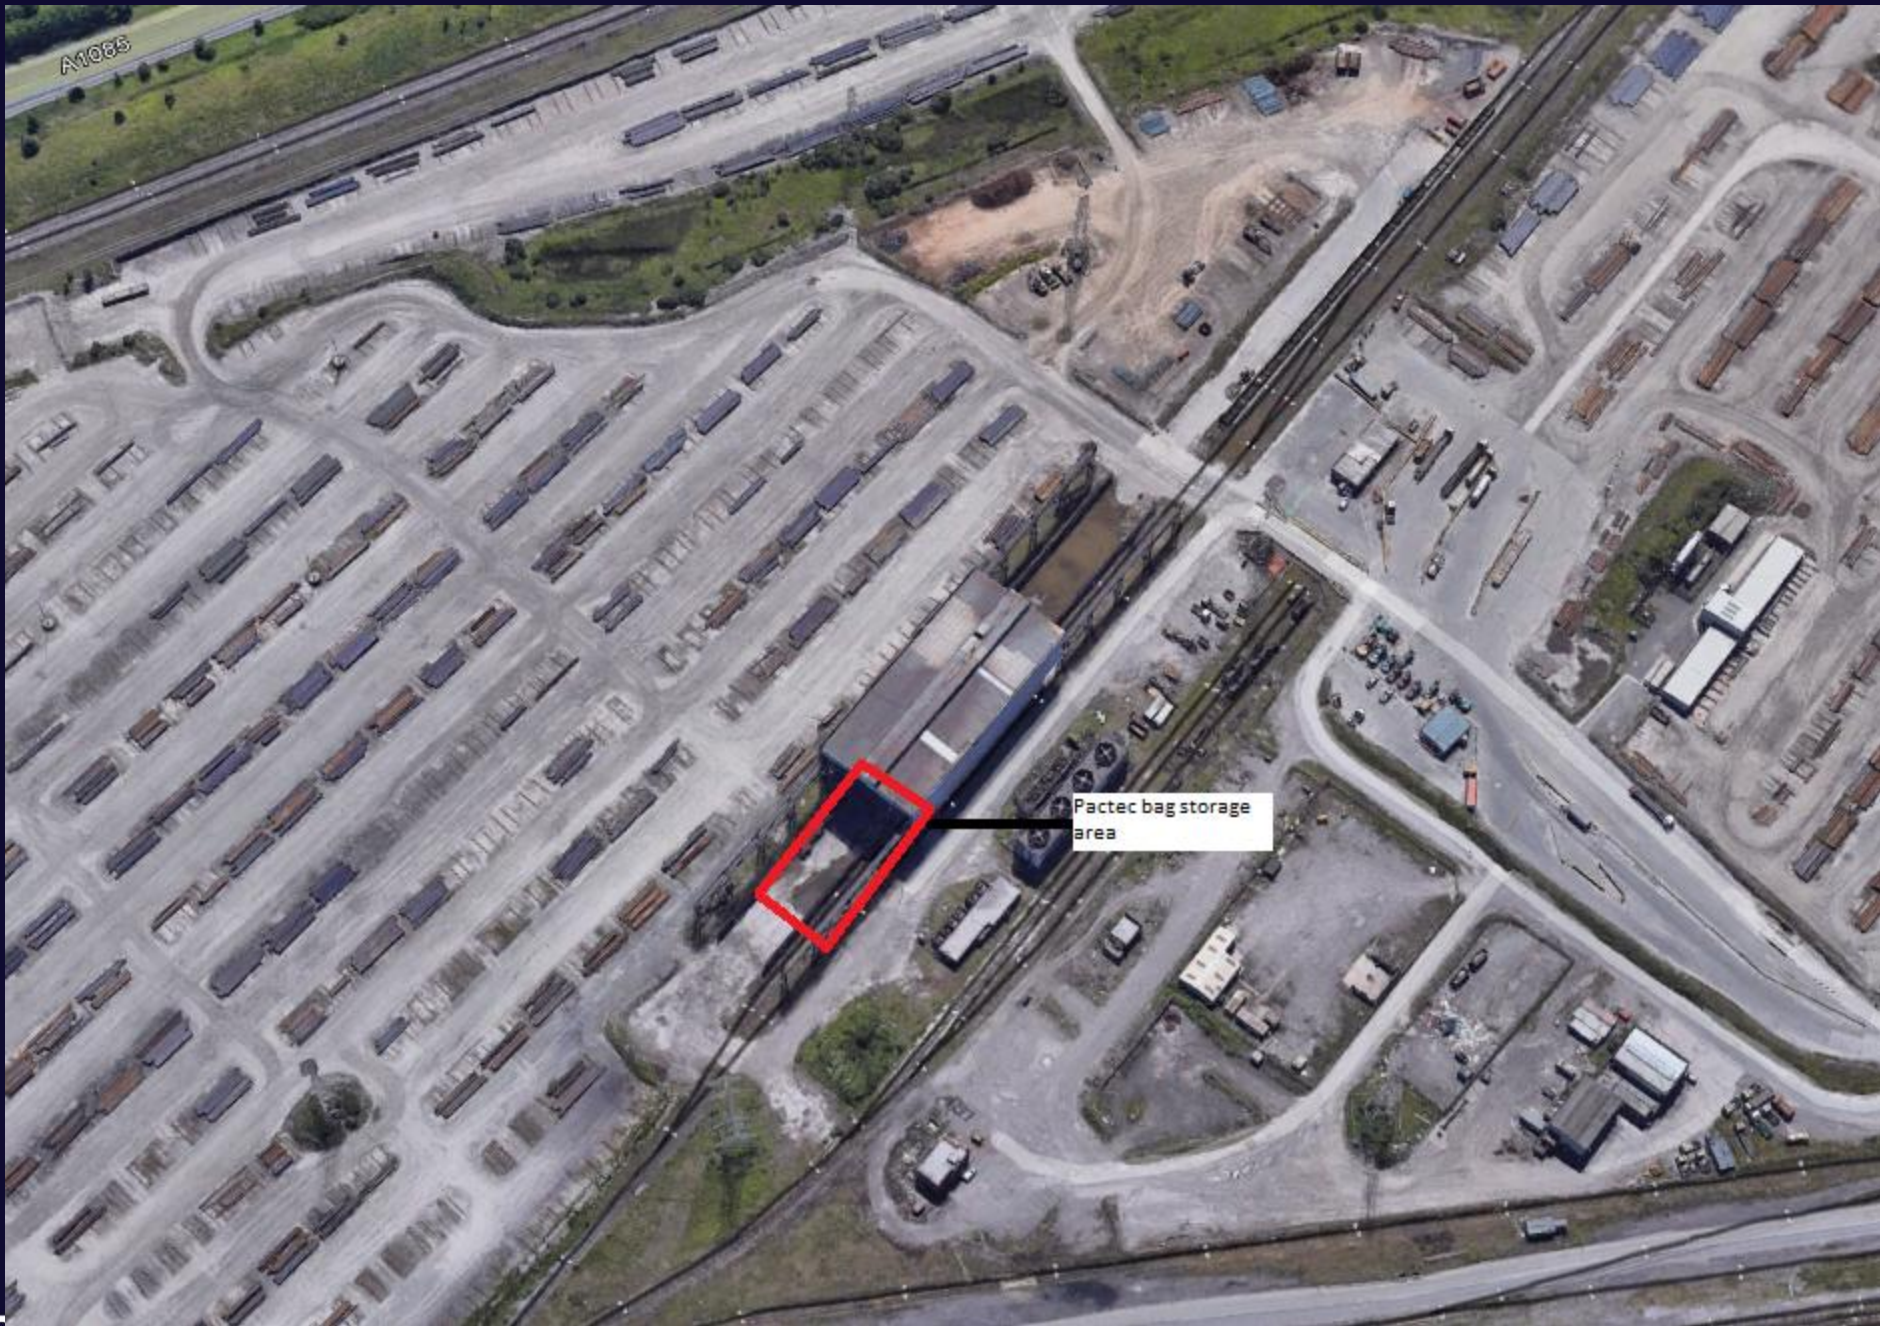

Arterial Mains

- Coke Oven Gas Section 8 (underground, Lackenby) now complete. Section 5 to complete. Standing water being extracted from Sections 7 and 8.
 - Material treated and stored in ASUK Waste Treatment Plant pending incineration offsite.
- Heavy Fuel Oil Section 1 now complete. Drawdown of material from Sections 3 and 4 in progress.

